
Pump House Upgrade

Classic Schedule Layout Data date 25-Jan-27

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
Pump House Upgrade		**35**	**25**	**04-Jan-27 A**	**19-Feb-27**	**0**
Engineering		**25**	**15**	**04-Jan-27 A**	**05-Feb-27**	**0**
A1000	Notice to proceed	0	0	04-Jan-27 A		
A1010	Design pump skid	10	0	04-Jan-27 A	15-Jan-27 A	
A1020	Procure pumps	15	10	18-Jan-27 A	05-Feb-27	0
A1080	Project management	30	20	04-Jan-27 A	12-Feb-27	5



Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
Construction		**19**	**19**	**25-Jan-27**	**19-Feb-27**	**0**
Mechanical		**18**	**18**	**25-Jan-27**	**18-Feb-27**	**1**
A1030	Demolish old skid	5	5	25-Jan-27	29-Jan-27	5
A1040	Set new pumps	4	4	08-Feb-27	11-Feb-27	0
A1050	Pipe and wire – Unit 2	6	6	10-Feb-27	18-Feb-27	1
A1060	Test and turnover	3	3	17-Feb-27	19-Feb-27	0
A1070	Ready for service	0	0		19-Feb-27	0

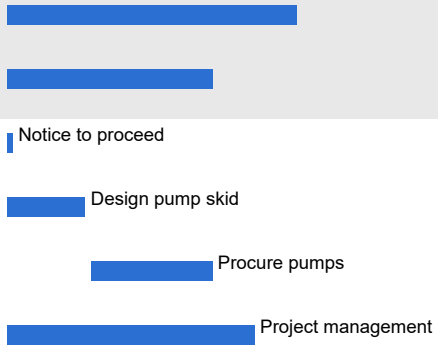
